



**21<sup>ST</sup> CENTURY SCHOOLS  
BOND ADVISORY COMMITTEE  
SEPTEMBER 10, 2013**



# AGENDA



- **Call to Order**
- **Welcome**
- **Approval of Minutes: June 11, 2013**
- **Legal Issues**
- **GOB Update:**
  - **Office of School Facilities**
    - GOB Project Dashboard
    - Update Year 1 Project Rollout
    - Update Year 2 Project Rollout
    - Five-Year Capital Plan
  - **Office of Financial Services**
    - Bond Sale Update
  - **Office of Economic Opportunity**
    - Outreach Activities
    - SBE/MBE Certification Statistics
    - M/WBE Disparity Study Update
  - **Sub-Committee Report**
  - **Discussion**
  - **New Business Section**
  - **Adjourn**




**LEGAL ISSUES  
SCHOOL BOARD ATTORNEY'S OFFICE  
(VERBAL REPORT)**



# GOB UPDATE OFFICE OF SCHOOL FACILITIES

# GOB PROJECT DASHBOARD



- In keeping with the GOB's guiding principle of creating and maintaining complete transparency, the District has developed a public Dashboard that will track the progress of GOB projects
- This Dashboard, will go live in September and will allow the general public to access GOB project related information through the District's main webpage as well as through each individual school's webpage
- The Dashboard provides easy to navigate screens that depict project information at a number of levels, e.g. district-wide, by region, by type of school, by Board member and by municipality
- Dashboard information includes project type, architect and contractor, budget, schedule and SBE/MWBE participation, and will be used to chronicle progress over the life of each project through a photo gallery
- To ensure information is current, the Dashboard will be updated frequently

# GOB PROJECT DASHBOARD SAMPLE PROGRAM-WIDE ROLLUP



## Miami-Dade County Public Schools Capital Projects Funded by the General Obligation Bond

Last Updated September 6, 2013

Projects			
☐ Region	Budgeted	Expended	Total Projects
☐ North	\$24,892,293	\$233	13
☐ Central	\$54,964,433	\$1,170	22
☐ South	\$45,799,446	\$219	25
☐ Education Transformation	\$46,748,728	\$16,122	7
☐ Other	\$1,508,959	\$0	1
☐ Board Member District			
☐ Municipality			
☐ School Type			
Grand Total: \$173,913,859      \$17,743      68			

### Schedule

Stage	Count
Planning	65
Design	3

### Financials

### MWBE

# GOB PROJECT DASHBOARD SAMPLE REGION-BASED SCHOOL DETAIL



Miami-Dade County Public Schools Capital Projects Funded by the General Obligation Bond						
Projects						
Region		Budgeted	Expended	Total Projects		
North		\$24,892,293	\$233	13		
Location	Project #	Budgeted	Expended	Scope	Status	
<a href="#">0241 - RUTH K BROAD/BAYHARBOR K-8</a>	01306000	\$1,039,009	\$233	GO Bond funded Rem/Ren project	Planning	
<a href="#">0321 - BISCAYNE ELEMENTARY</a>	01301400	\$2,472,795	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">0581 - W.J. BRYAN ELEMENTARY</a>	01307200	\$1,401,819	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">2081 - FULFORD ELEMENTARY</a>	01303400	\$2,452,748	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">2441 - VIRGINIA ABOONE/HIGHLAND OAKS</a>	01307100	\$2,219,768	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">3741 - NORTH BEACH ELEMENTARY</a>	01305400	\$1,882,973	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">4241 - PALM LAKES ELEMENTARY</a>	01305600	\$1,431,002	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">4801 - GERTRUDE EDELMAN/SABAL PALM EL</a>	01303500	\$2,531,888	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">6241 - HIGHLAND OAKS MIDDLE</a>	01304200	\$1,242,388	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">7141 - DR MICHAEL M KROP SENIOR HIGH</a>	01302300	\$1,060,411	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">7391 - MIAMI LAKES EDUCATIONAL CENTER</a>	01305200	\$2,492,821	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">8101 - JAN MANN OPPORTUNITY SCHOOL</a>	01304300	\$2,025,947	\$0	GO Bond funded Rem/Ren project	Planning	
<a href="#">8151 - ROBERT RENICK EDUCATION CTR</a>	01305900	\$2,838,948	\$0	GO Bond funded Rem/Ren project	Planning	
<b>North Total:</b>		<b>\$24,892,293</b>	<b>\$233</b>	<b>13</b>		
Central		\$54,964,433	\$1,170	22		
South		\$45,799,446	\$219	25		
Education Transformation		\$46,748,728	\$16,122	7		
Other		\$1,508,959	\$0	1		
Board Member District						
Municipality						
School Type						
<b>Grand Total:</b>		<b>\$173,913,859</b>	<b>\$17,743</b>	<b>68</b>		


Schedule	
Planning	65
Design	3

Financials	
MWBE	

# GOB PROJECT DASHBOARD SAMPLE

## SCHOOL TYPE DETAIL



**Miami-Dade County Public Schools**  
**Capital Projects Funded by the**  
**General Obligation Bond**

Last Updated September 6, 2013

**Projects**

☐ Region	Budgeted	Expended	Total Projects	
☐ North	\$24,892,293	\$233	13	
☐ Central	\$54,964,433	\$1,170	22	
☐ South	\$45,799,446	\$219	25	
☐ Education Transformation	\$46,748,728	\$16,122	7	
☐ Other	\$1,508,959	\$0	1	
☐ Board Member District				
☐ Municipality				
☐ School Type				
☐ Elementary	\$76,677,693	\$80	40	40
☐ K8 Center	\$17,950,508	\$698	10	9
☐ Middle	\$7,059,946	\$0	4	4
☐ Senior	\$66,582,702	\$16,826	11	11
☐ Educational Center	\$4,134,051	\$139	2	2
☐ Vocational/Adult	\$1,508,959	\$0	1	1
<b>Grand Total:</b>	<b>\$173,913,859</b>	<b>\$17,743</b>	<b>68</b>	

**Schedule**

Status	Count
Planning	65
Design	3

**Financials**

**MWBE**



# GOB PROJECT DASHBOARD SAMPLE BOARD MEMBER DISTRICT DETAIL



## Miami-Dade County Public Schools Capital Projects Funded by the General Obligation Bond


Last Updated September 6, 2013

### Projects

Region		Budgeted	Expended	Total Projects	
<input checked="" type="checkbox"/>	North	\$24,892,293	\$233	13	
<input checked="" type="checkbox"/>	Central	\$54,964,433	\$1,170	22	
<input checked="" type="checkbox"/>	South	\$45,799,446	\$219	25	
<input checked="" type="checkbox"/>	Education Transformation	\$46,748,728	\$16,122	7	
<input checked="" type="checkbox"/>	Other	\$1,508,959	\$0	1	
Board Member District					
<input checked="" type="checkbox"/>	1 - Dr. Wilbert "Tee" Holloway	\$42,941,946	\$16,122	5	
Location	Project #	Budgeted	Expended	Scope	Status
<a href="#">0561 - W.J. BRYAN ELEMENTARY</a>	01307200	\$1,401,819	\$0	GO Bond funded Rem/Ren project	Planning
<a href="#">4121 - DR. ROBERT B. INGRAM EL</a>	01302700	\$1,875,232	\$0	GO Bond funded Rem/Ren project	Planning
<a href="#">7381 - MIAMI NORLAND SENIOR HIGH</a>	00223200	\$35,000,000	\$16,122	School Replacement. No net gain in student stations.	Design
<a href="#">8101 - JAN MANN OPPORTUNITY SCHOOL</a>	01304300	\$2,025,947	\$0	GO Bond funded Rem/Ren project	Planning
<a href="#">8151 - ROBERT RENICK EDUCATION CTR</a>	01305900	\$2,638,948	\$0	GO Bond funded Rem/Ren project	Planning
<b>1 - Dr. Wilbert "Tee" Holloway Total:</b>		<b>\$42,941,946</b>	<b>\$16,122</b>	<b>5</b>	

# GOB PROJECT DASHBOARD SAMPLE COUNTY/MUNICIPALITY DETAIL



 <b>Miami-Dade County Public Schools Capital Projects Funded by the General Obligation Bond</b>				Last Updated September 6, 2013		
Projects						
<input type="checkbox"/> Region	Budgeted	Expended	Total Projects			
<input type="checkbox"/> North	\$24,892,293	\$233	13			
<input type="checkbox"/> Central	\$54,964,433	\$1,170	22			
<input type="checkbox"/> South	\$45,799,446	\$219	25			
<input type="checkbox"/> Education Transformation	\$46,748,728	\$16,122	7			
<input type="checkbox"/> Other	\$1,508,959	\$0	1			
<input type="checkbox"/> Board Member District						
<input type="checkbox"/> Municipality						
<input type="checkbox"/> North Miami	\$1,401,819	\$0	1			
<input type="checkbox"/> Opa-Locka	\$1,875,232	\$0	1			
<input type="checkbox"/> Miami Gardens	\$39,664,895	\$16,122	3			
<input type="checkbox"/> Miami	\$17,772,735	\$0	10			
<input type="checkbox"/> Miami Beach	\$4,355,768	\$0	2			
<input type="checkbox"/> North Miami Beach	\$2,452,748	\$0	1			
<input type="checkbox"/> Bay Harbor Islands	\$1,039,009	\$233	1			
<input type="checkbox"/> Unincorporated Miami-Dade	\$76,886,895	\$923	34			
<input type="checkbox"/> Hialeah	\$4,908,119	\$0	3			
<input type="checkbox"/> Miami Lakes	\$2,492,821	\$0	1			
<input type="checkbox"/> South Miami	\$2,584,512	\$0	1			
<input type="checkbox"/> Key Biscayne	\$4,021,024	\$466	2			
<input type="checkbox"/> Coral Gables	\$1,595,039	\$0	1			
<input type="checkbox"/> Cutler Bay	\$5,344,317	\$0	3			
<input type="checkbox"/> Palmetto Bay	\$3,905,517	\$0	2			
<input type="checkbox"/> Homestead	\$3,613,409	\$0	2			
<input type="checkbox"/> School Type						
<b>Grand Total:</b>				\$173,913,859	\$17,743	68
Schedule						

# GOB PROJECT DASHBOARD INDIVIDUAL SCHOOL DASHBOARD



PROJECT # 01307200  
0561 - W.J. BRYAN ELEMENTARY  
1201 NE 125 th Street, North Miami

School Board District 1  
Dr. Wilbert "Tee" Holloway

North

Last Updated September

## SCOPE

GO Bond funded Rem/Ren project

[W.J. BRYAN ELEMENTARY WEBSITE](#)


## GENERAL INFORMATION

Project Type	Renovation
Project ID	01307200
Student Stations	0
Architect	Stantec Consulting Services, Inc.
Contractor	Kalex Construction & Development
Delivery Method	CM @ Risk Misc.
Small Business Participation	----
Minority & Women Business Participation	----
Status	Planning



## SCHEDULE

Milestone	Projected	Actual	Completion
Planning	08/26/2013		
Start Design	08/27/2013		
Complete Design	04/16/2014		
Start Construction	07/22/2014		
Complete Construction	10/15/2015		
Occupancy			



\*\* Tentative dates; actual schedule is being finalized. \*\*

## FINANCIALS

Budget	\$1,401,819.00
Complete	0%
Expended	\$0.00
Balance	\$1,401,819.00



PROJECT # 01305300  
3501 - MORNINGSIDE K-8 ACADEMY  
6620 NE 5th Avenue, Miami

School Board District 2  
Dr. Dorothy Bendross-Mindingall

Education Transformation Region  
Last Updated September 6, 2013

## SCOPE

GO Bond funded Rem/Ren project

[MORNINGSIDE K-8 ACADEMY WEBSITE](#)


## GENERAL INFORMATION

Project Type	Renovation
Project ID	01305300
Student Stations	0
Architect	Livs Associates
Contractor	Mcm Corporation
Delivery Method	CM @ Risk Misc.
Small Business Participation	----
Minority & Women Business Participation	----
Status	Planning



## SCHEDULE


Milestone	Projected	Actual	Completion
Planning	08/24/2013		
Start Design	08/25/2013		
Complete Design	04/14/2014		
Start Construction	07/20/2014		
Complete Construction	10/13/2015		
Occupancy			




\*\* Tentative dates; actual schedule is being finalized. \*\*

## FINANCIALS

Budget	\$2,149,162.00
Complete	0%
Expended	\$0.00
Balance	\$2,149,162.00



# GOB PROJECT DASHBOARD INDIVIDUAL SCHOOL DASHBOARD



**PROJECT # 01307100**  
2441 - VIRGINIA A BOONE/HIGHLAND OAKS  
20500 NE 24th Avenue, Miami

School Board District 3  
Dr. Martin S. Karp, Vice-Chair

Last Updated September 6, 2013

## SCOPE

GO Bond funded RemiRen project

[VIRGINIA A BOONE/HIGHLAND OAKS WEBSITE](#)


## GENERAL INFORMATION

Project Type	Renovation
Project ID	01307100
Student Stations	0
Architect	Rodriguez Architects, Inc.
Contractor	T & G Constructors
Delivery Method	CM @ Risk Misc.
Small Business Participation	---
Minority & Women Business Participation	---
Status	Planning



## SCHEDULE

Milestone	Projected	Actual	Completion
Planning	08/26/2013		
Start Design	08/27/2013		
Complete Design	04/16/2014		
Start Construction	07/22/2014		
Complete Construction	10/15/2015		
Occupancy			



\*\* Tentative dates; actual schedule is being finalized. \*\*

## FINANCIALS

Budget	\$2,219,766.00
Complete	0%
Expended	\$0.00
Balance	\$2,219,766.00



**PROJECT # 01305200**  
7391 - MIAMI LAKES EDUCATIONAL CENTER  
5780 NW 158 Street, Miami Lakes

School Board District 4  
Ms. Perla Tabares Hantman, Chair

North Region  
Last Updated September 6, 2013

## SCOPE

GO Bond funded RemiRen project

[MIAMI LAKES EDUCATIONAL CENTER WEBSITE](#)


## GENERAL INFORMATION

Project Type	Renovation
Project ID	01305200
Student Stations	0
Architect	M. C. Harry & Associates, Inc.
Contractor	Link Construction Group Inc
Delivery Method	CM @ Risk Misc.
Small Business Participation	---
Minority & Women Business Participation	---
Status	Planning



## SCHEDULE

Milestone	Projected	Actual	Completion
Planning	08/24/2013		
Start Design	08/25/2013		
Complete Design	04/14/2014		
Start Construction	07/20/2014		
Complete Construction	10/13/2015		
Occupancy			



\*\* Tentative dates; actual schedule is being finalized. \*\*

## FINANCIALS

Budget	\$2,492,821.00
Complete	0%
Expended	\$0.00
Balance	\$2,492,821.00



# GOB PROJECT DASHBOARD INDIVIDUAL SCHOOL DASHBOARD



**PROJECT # 01304500**  
**2781 - KINLOCH PARK ELEMENTARY**  
4275 NW 1st Street, Miami

School Board District 5  
Ms. Susie V. Castillo

Last Updated S

---

**SCOPE**

GOB: Roofing, Group Toilets, Electrical, Paint

[KINLOCH PARK ELEMENTARY WEBSITE](#)

---

**GENERAL INFORMATION**

Project Type	Renovation
Project ID	01304500
Student Stations	0
Architect	Urs Corporation Southern
Contractor	Veitia Padron Inc
Delivery Method	CM @ Risk Misc.
Small Business Participation	----
Minority & Women Business Participation	----
Status	Planning

---

**SCHEDULE**

Milestone	Projected	Actual	Completion
Planning	08/12/2013		
Start Design	08/28/2013		
Complete Design	07/06/2014		
Start Construction	10/12/2014		
Complete Construction	10/07/2015		
Occupancy			

\*\* Tentative dates; actual schedule is being finalized. \*\*

---

**FINANCIALS**

Budget	\$2,538,315.00
Complete	0%
Expended	\$0.00
Balance	\$2,538,315.00

Budget Availability

100% 0%

% Balance % Expended

**PROJECT # 01300800**  
**0121 - AUBURDALE ELEMENTARY**  
3255 SW 6th Street, Miami

School Board District 6  
Ms. Raquel A. Regalado

Central Region  
Last Updated September 6, 2013

---

**SCOPE**

GO Bond funded Rem/Ren project

[AUBURDALE ELEMENTARY WEBSITE](#)

---

**GENERAL INFORMATION**

Project Type	Renovation
Project ID	01300800
Student Stations	0
Architect	Csa Central, Inc.
Contractor	Grace & Naeem Uddin Inc
Delivery Method	CM @ Risk Misc.
Small Business Participation	----
Minority & Women Business Participation	----
Status	Planning

---

**SCHEDULE**

Milestone	Projected	Actual	Completion
Planning	08/25/2013		
Start Design	08/26/2013		
Complete Design	04/15/2014		
Start Construction	07/21/2014		
Complete Construction	10/14/2015		
Occupancy			

\*\* Tentative dates; actual schedule is being finalized. \*\*

---

**FINANCIALS**

Budget	\$2,441,947.00
Complete	0%
Expended	\$0.00
Balance	\$2,441,947.00

Budget Availability

100% 0%

% Balance % Expended

# GOB PROJECT DASHBOARD

## INDIVIDUAL SCHOOL DASHBOARD



**PROJECT # 01306600**  
**5281 - SOUTH MIAMI HEIGHTS ELEMENTARY**  
 12231 SW 190th Terrace, Miami

School Board District 7  
 Mr. Carlos L. Curbelo

Last Updated

**PROJECT # 01306900**  
**5641 - VILLAGE GREEN ELEMENTARY**  
 12265 SW 34th Street, Miami

School Board District 8  
 Dr. Marta Pérez

South Region  
 Last Updated September 6, 2013

**SCOPE**  
 GO Bond funded Rem/Ren project

**SCOPE**  
 GO Bond funded Rem/Ren project

**GENERAL INFORMATION**

**GENERAL INFORMATION**



Project Type	Renovation
Project ID	01306600
Student Stations	0
Architect	Rizo Carreno & Partners, Inc.
Contractor	D. Stephenson Construction, Inc.
Delivery Method	CM @ Risk Misc.
Small Business Participation	----
Minority & Women Business Participation	----
Status	Planning

Project Type	Renovation
Project ID	01306900
Student Stations	0
Architect	Saltz Michelson Architects, Inc.
Contractor	Coastal Construction Company
Delivery Method	CM @ Risk Misc.
Small Business Participation	----
Minority & Women Business Participation	----
Status	Planning



**SCHEDULE**

**SCHEDULE**



\*\* Tentative dates; actual schedule is being finalized. \*\*


\*\* Tentative dates; actual schedule is being finalized. \*\*

**FINANCIALS**

**FINANCIALS**

Budget	\$2,171,947.00
Complete	0%
Expended	\$0.00
Balance	\$2,171,947.00

Budget	\$2,375,371.00
Complete	0%
Expended	\$0.00
Balance	\$2,375,371.00



# GOB PROJECT DASHBOARD INDIVIDUAL SCHOOL DASHBOARD



**PROJECT # 01303300**  
**3101 - FRANK C. MARTIN K-8 CENTER**  
 14250 Boggs Drive, Miami

School Board District 9  
Dr. Lawrence S. Feldman
South Region  
Last Updated September 6, 2013

---

**SCOPE**

GO Bond funded Rem/Ren project [FRANK C. MARTIN K-8 CENTER WEBSITE](#)

---

**GENERAL INFORMATION**

Project Type	Renovation
Project ID	01303300
Student Stations	0
Architect	Sblm Architects, Pc
Contractor	Stobs Bros. Construction Company
Delivery Method	CM @ Risk Misc.
Small Business Participation	----
Minority & Women Business Participation	----
Status	Planning

---

**SCHEDULE**

Milestone	Projected	Actual	Completion
Planning	09/01/2013		
Start Design	09/02/2013		
Complete Design	04/22/2014		
Start Construction	07/28/2014		
Complete Construction	10/21/2015		
Occupancy			

\*\* Tentative dates; actual schedule is being finalized. \*\*


---

**FINANCIALS**

Budget	\$2,469,872.00
Complete	0%
Expended	\$0.00
Balance	\$2,469,872.00

- ## Public Dashboard Features:
- Easy to navigate
  - Readily accessible through the District's website or individual school's webpage
  - Tracks progress of projects as to cost and schedule
  - Promotes transparency and accountability

# YEAR-1 PROJECT ROLLOUT UPDATE



- Since the June 11, 2013 GOB Advisory Committee meeting, the District has expanded the cadre of design professionals and construction managers for projects with construction values up to \$2M
- 19 design professionals and 16 construction managers commissioned
- The 66 Year -1 projects with estimated construction values of \$2M or less have now all been assigned to these design professionals and construction managers based on the following protocol:
  - Projects were grouped geographically to maximize operational and mobilization efficiencies
  - Number of projects assigned to each design professional and contractor was based on each firm's ranking during RFQ evaluation
  - More experienced design professionals were paired with construction managers having less experience with the District, and vice-versa
  - School site kick-off meetings started on August 22, 2013




# YEAR-1 PROJECT ROLLOUT UPDATE



- Year-1 project roll out next steps:
  - Continue coordination with District Instructional Technology staff regarding backbone upgrades and wireless technology deployment
  - Complete kick-off meetings at remaining schools by October 2, 2013
  - Receive final scope, estimate and proposed schedule from Design professionals for each project
  - Issue a notice to proceed to each project architect and contractor, upon approval of scope, estimate and schedule by the District
- Based on this protocol, project design activities are expected to start in late September 2013
- Design/plan review phase is expected to take 4 to 6 months, depending on project complexity
- Construction work will be phased to minimize disruption of schools and is expected to commence in Spring 2014

# YEAR-2 PROJECT ROLLOUT UPDATE




- Year-2 (FY 2013-14) includes 79 projects of varying size and complexity:
  - Approximately 61 projects are candidates for Small Business Enterprise (SBE) and Micro Business Enterprise (MBE) firms
  - Two solicitations for proposals from eligible SBE/MBE architects, engineers and construction management firms, have been advertised for projects with construction values under \$1M
  - Larger projects will be subject to project-specific solicitations
- The SBE Advisory Committee (SBEAC) is finalizing its review of District selection procedures for architects, engineers and construction managers to ensure alignment with newly adopted Board policy on SBE
- Revised selection procedures are expected to be presented to the School Board for approval in October

# YEAR-2 PROJECT ROLLOUT UPDATE


- Responses to competitive solicitations from eligible SBE/MBE architects/engineers and construction management firms will be accepted in November
- It is expected that SBE/MBE construction management firms can be prequalified beginning in December 2013
- School Board commissioning of qualified SBE/MBE firms is expected to be completed by early 2014
- Assignment of Year-2 projects under \$1M will follow the commissioning process following a protocol similar to Year-1
- Competitive solicitations for larger projects will be advertised once the disparity study is completed, M/WBE Policy is adopted by the Board and relevant selection procedures are updated

# FIVE-YEAR CAPITAL PLAN



- The District's Five-Year Capital Work Plan (Plan) was unanimously approved by the School Board at its final budget public hearing held on September 3<sup>rd</sup>
- The Plan includes projects funded in Fiscal Year 2013-14 through and including Fiscal Year 2017-18
- Year-1 GOB projects are shown in the Plan as "carry-forward" since they were approved by the Board on May 8, 2013 for funding in Fiscal Year 2012-13, as reported to the Committee at its June 11, 2013 meeting
- The Plan reflects and respects all previous commitments to touch every school in a meaningful way, including technology upgrades

# FIVE-YEAR CAPITAL PLAN



- Project allocations have prioritized critical deficiency needs
- In the case of proposed replacements, campus right-sizing was based on current and projected student enrollment
- The GOB program delivery has been compressed to a total of five years (including FY 2012-13)
- As previously endorsed by the 21<sup>st</sup> Century Schools Bond Advisory Committee, select projects were advanced from later years to FY 2013-14

The Plan may be accessed at:

[Agenda Item E-15](#)

[E-15 Supplemental Information](#)




**GOB UPDATE  
OFFICE OF FINANCIAL SERVICES  
(VERBAL REPORT)**



# GOB UPDATE

## OFFICE OF ECONOMIC OPPORTUNITY

# OUTREACH ACTIVITIES



- **M-DCPS EVENTS:**

- Prequalification Certification Workshop

- **OTHER EVENTS ATTENDED:**

- Miami-Dade Chamber of Commerce – Construction Industry Group Meeting
  - Doral Business Council Monthly Meeting
  - Miami Dade County –Minority Affairs Division (Aviation) Monthly Meeting
  - South Florida Minority Supplier Development Council-Construction Industry Group Meeting

- **UPCOMING EVENTS:**


- Miami-Dade Chamber of Commerce - Business Women’s Council
  - Opa-Locka Chamber of Commerce
  - Aventura Marketing Council
  - Breakfast with the Director

- **EVENTS BEING PLANNED:**


- Hialeah Chamber of Commerce
  - Latin Builders Association




# SBE/MBE CERTIFICATION STATISTICS 2013-2014



## 2013/2104 SBE/MBE CERTIFICATION

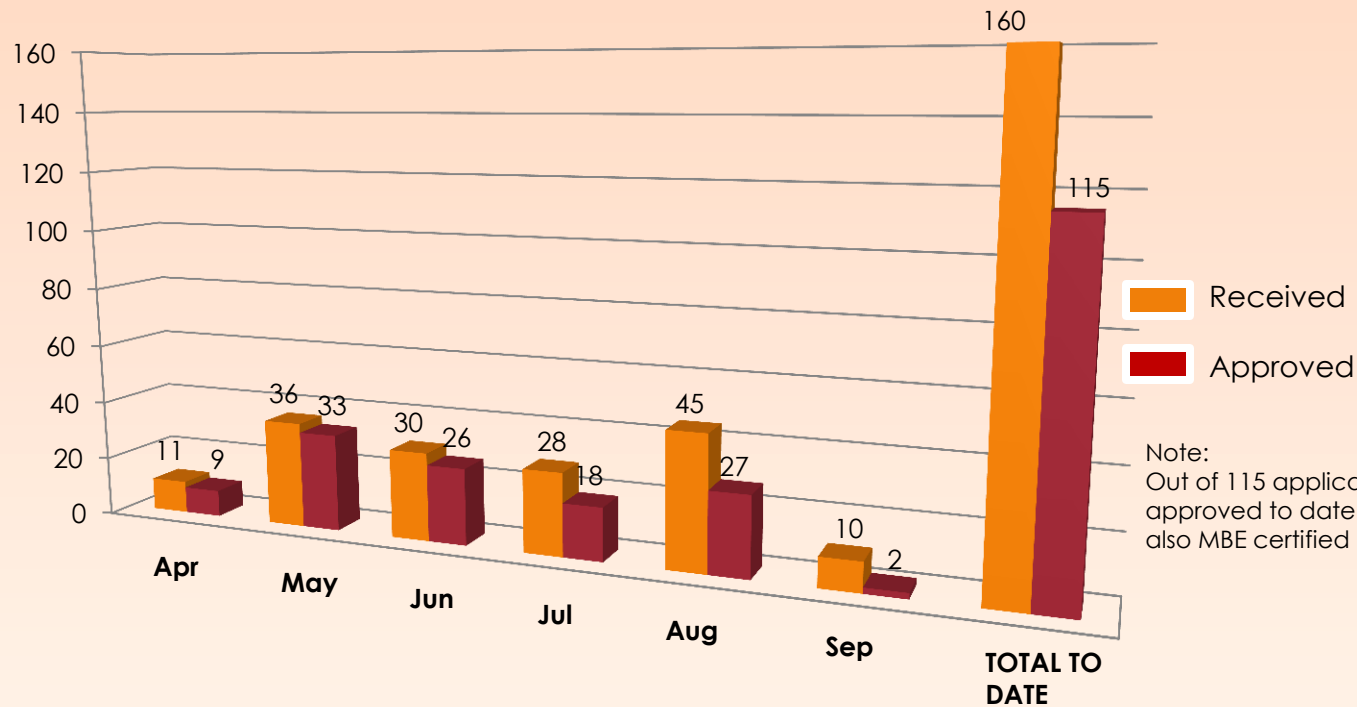

# M/WBE DISPARITY STUDY UPDATE




## Key Dates:

- **September 2013**
  - Results received from consultant (MGT)
- **October 2013**
  - Conduct School Board Workshop
  - Review of M/WBE Policy by advisory committee
- **November 2013**
  - Present findings to School Board
  - Initial reading of M/WBE Policy



# GOB UPDATE OUTREACH SUB-COMMITTEE REPORT (VERBAL)



# GOB DISCUSSION



## GOB - NEW BUSINESS



**NEXT ADVISORY COMMITTEE MEETING:  
DECEMBER 10, 2013, 3:00 TO 5:00 P.M.**
